


ID	Task Name	Duration	Start	Finish	August							September				
					7/23	7/30	8/6	8/13	8/20	8/27	9/3	9/10				
1	32 Marion Street - Demo and Abatement	23 days	Mon 7/31/23	Wed 8/30/23												
2	Abatement	5 days	Mon 7/31/23	Fri 8/4/23												
3	Abatement Roof 4-5	2 days	Mon 7/31/23	Tue 8/1/23												
4	Abatement Roof 1-2-3	2 days	Wed 8/2/23	Thu 8/3/23												
5	Abatement Roof 6-7	2 days	Thu 8/3/23	Fri 8/4/23												
6	Demo	19 days	Fri 8/4/23	Wed 8/30/23												
7	Demolition Permit Receipt	1 day	Fri 8/4/23	Fri 8/4/23												
8	Building Truck Wash	2 days	Mon 8/7/23	Tue 8/8/23												
9	Demo 4-5	6 days	Mon 8/7/23	Mon 8/14/23												
10	Demo 1-2-3	12 days	Tue 8/15/23	Wed 8/30/23												

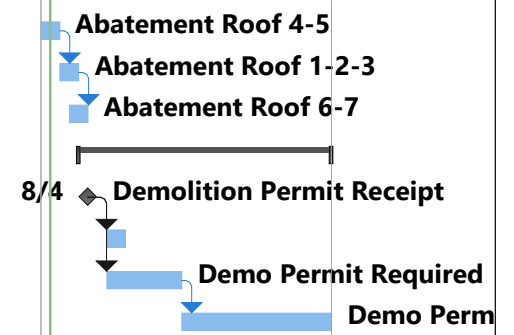

Project: 32 Marion Street - Dem Date: Tue 8/1/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
